Exhibit B: Project Schedule

Natividad Medical Center
Radiology Modernization Construction Schedule
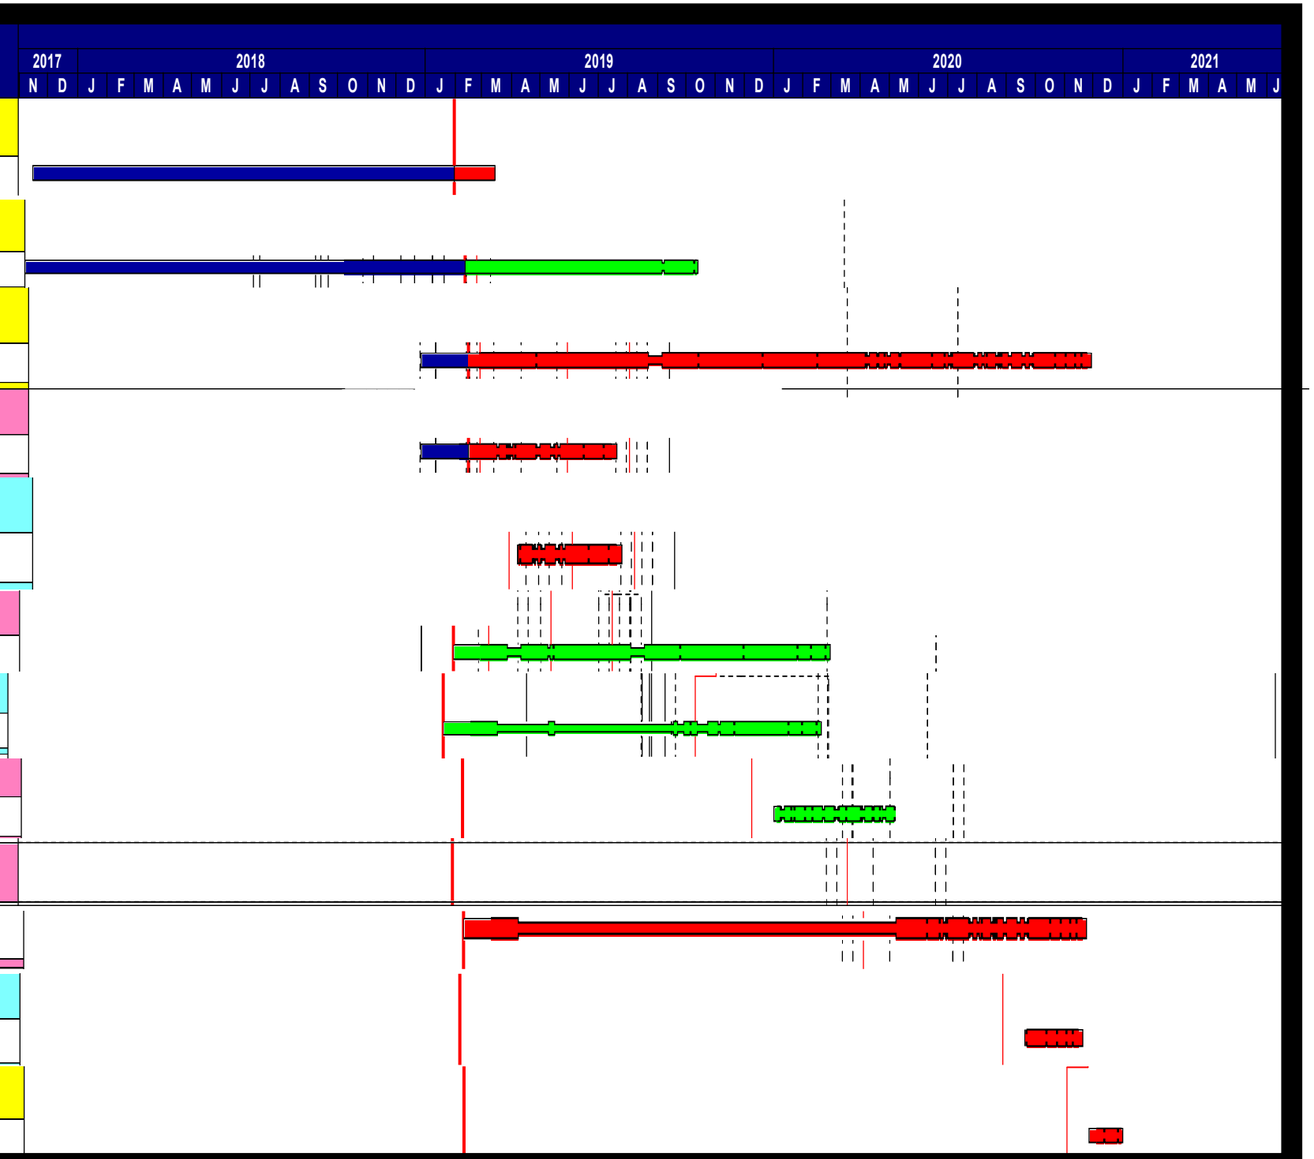
Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	Total Float	Predecessors	Successors
Preconstruction								
		339d	31d	15NOV17 A	15MAR19	-6d		
Medical Equip & OSHPD DA's								
		513d	169d	26SEP17 A	30SEP19	246d		
Construction								
		479d	449d	13DEC18 A	09NOV20	-34d		
Phase 1: Make Ready, Temp dressing & Hot Lab								
		139d	109d	13DEC18 A	05JUL19	-6d		
Chiller & Pad								
		78d	78d	18MAR19	05JUL19	-6d		
Phase 2: MRI, Nuc Med, Angio..								
		274d	274d	31JAN19	04MAR20	141d		
Phase 2a: Hot Lab..								
		274d	274d	31JAN19	04MAR20	141d		
Phase 3: Dress, Toilets, Staff								
		86d	86d	19DEC19	23APR20	105d		
Phase 4: CT Scan 2 & Ultrasound								
		449d	449d	31JAN19	09NOV20	-34d		
Phase 4a: Corridors								
		44d	44d	09SEP20	09NOV20	-59d		
Project Closeout								
		25d	25d	10NOV20	16DEC20	-59d
